


TSM&O Summary Report – July 2026

Highlights


- Coordinated with Project Managers and CEI for various closures. Created all pre-event and construction messaging plans for: I-395/SR 836/I-95 Design-Build, Golden Glades Interchange Enhancement Project, Wrong Way Driving Detection System (Multiple Locations), Express Lane Tubular Marker Maintenance, ITS Device Replacement Projects, US 27/SR 25/Okeechobee Road Projects, US 1 Keys Construction (Multiple Projects), and Florida Keys Aqueduct Authority Water Main Repair
- Provided support for the 2026 FIFA World Cup at Miami Stadium
- Adjusted signal timing along U.S. 1 in Monroe County due to Fourth of July holiday and Lobster Mini-Season
- Successfully reinstated tolling for Palmetto Express
- Hosted special National TIM Responder sessions to help local towing companies comply with new training requirement

TMC Operations


Secondary Events Managed by Event Type

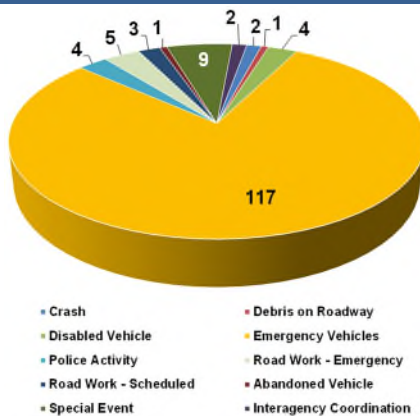

Event Summary Statistics

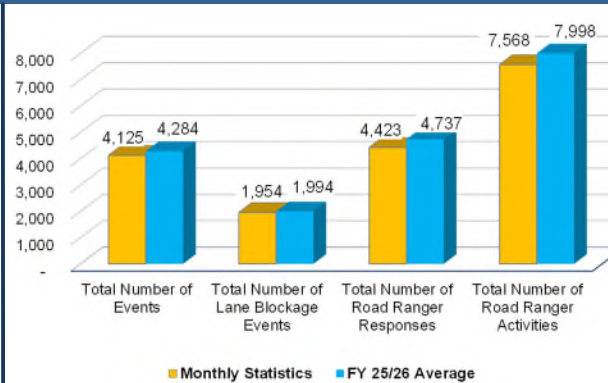

DMS Usage Summary

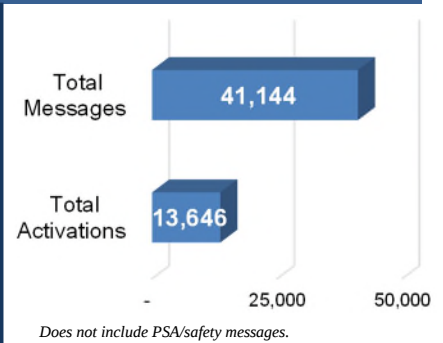


Backup Location Test ☒

TMC Operations Performance

Performance Measure	Non-Toll General Use Lanes		Express Lanes	
	July 2026	Target	July 2026	Target
DMS Efficiency (Lane Blockage)**	99.88%	≥95%	100%	100%
TMC Operator Error Rate (Lane Blockage)**	0.14	≤0.20	0.03	≤0.10
TMC Operator Error Rate (Non-Lane Blockage)	0.04	≤0.20	0.07	≤0.10
Road Ranger Dispatching Average (Lane Blockage)	0:00:25	≤0:02:00	0:00:18	≤0:00:60
Event Confirmation Average (Lane Blockage)	0:01:55	≤0:02:00	0:00:35	≤0:00:60
Time to Post DMS Average (Lane Blockage)	0:01:10	≤0:03:00	0:01:05	≤0:01:30
Agency Notification Average (Lane Blockage)	0:01:12	≤0:07:00	0:01:04	≤0:04:00




**As of June 1, 2021, values are computed from randomized sampling for lane blockage events.

Incident Management Performance



Active Arterial Management

Monroe County Traffic Signal System (MCTSS) from MM 0.0 to MM 106.5 Monday – Friday from 7:00 am - 7:00 pm

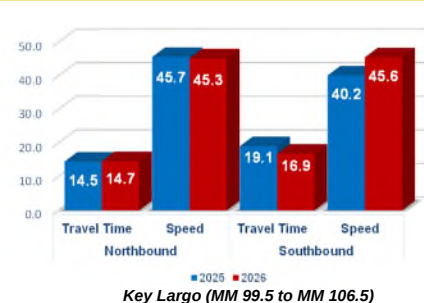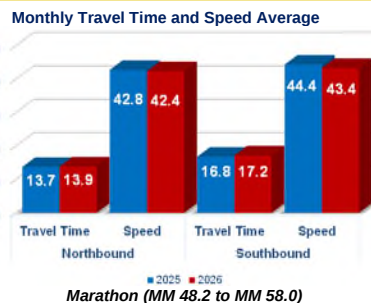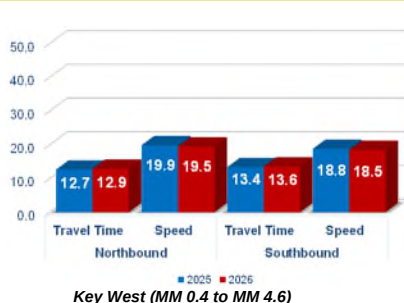

Systems Maintenance

ITS System Availability (FDOT Non-Operational)

Subsystem	July 2026	Target
TMC Systems (critical)	99.9%	≥99.9%
TMC Systems (non-critical)	99.5%	≥98.0%
www.sunguide.info	99.3%	≥98.0%

